

## Public Rights of Way

Work continues with diverting existing Public Rights of Ways (PRoWs) and creating new ones on and around the site. Photographs of the progress are shown below.

Footbridges over existing ditches are due to be installed over the coming weeks.

1.



Footpaths cut to correct depth.

2.




Drainage ditch management, including silt fencing either side.

3.



Base material laid.

4.

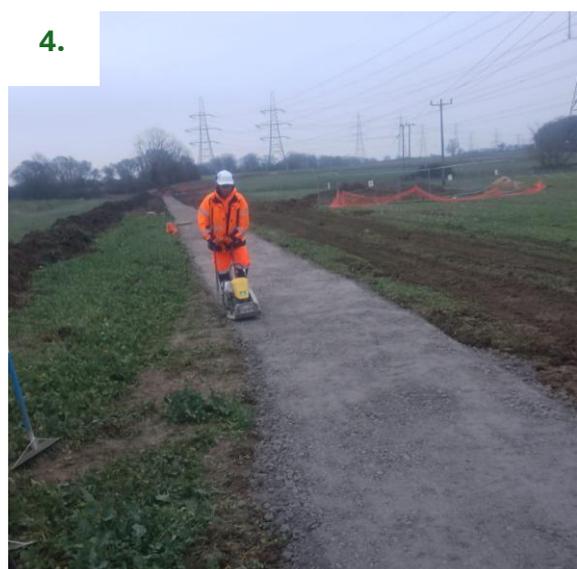

Final surface laid and compacted.
